

INVENTORY SYSTEM

PROJECT			
PROJECTID	CODE	NAME	CLIENT/CONSULTANT
23	632	HRRL	HRRL/EIL

DPR – DAILY PROGRESS REPORT

PROJECT INDEX				COSTING INDEX				PLANNING INDEX			BILLING INDEX				DELIVERY INDEX		
PROJECTDET				PROJECTMASTER-BPM				BBU BILLING BREAKUP				PROCESS	KANBAN				
PROJECTDETIC	BOQ NO	BBU/BOQ ITEM	DEPARTMENT/DISCIPLINE	QTY	UNIT	RATE	BBU AMOUNT	WTG	PLANSTART	PLANEND	DURATION	RABILL1	RABILL2	RABILL3	RABILL4	STARTDOC	
1	1.1	DRAWING	ENGINEERING/PROCESS	1	DWG	300000	300000	0.1	01-01-2023	01-02-2023		31	CODE2-55%	CODE1-25%	COMM-10%	COMP-10%	REVISION
2	1.2	DOSING PUMP	PROCUREMENT/MECHANICAL	10	NOS	10000	100000	0.2	02-02-2023	20-03-2023		40	PO-30%	MIR-50%	COMM-10%	COMP-10%	PO
3	1.4	VESSEL	MANUFACTURING/FACTORY	1	NOS	100000	100000	0.2	01-04-2023	10/4/20203		10	WO-30%	MIR-50%	COMM-10%	COMP-10%	MO
4	1.3	FOUNDATION	CONSTRUCTION/CIVIL	100	SQFT	3000	300000	0.4	01-04-2023	10/4/20203		10	STRUC-40%	RCC-30%	INSTALL-30%	COMP-10%	CO
5	1.5	VESSEL	ERECTION/COMMISSIONING	1	NOS	50000	50000	0.1	10-04-2023	20-04-2023		10	POWER-50%	TEST-30%	WORKING-5%	COMP-15%	CM
TOTAL							800000	1			101	PROFORMA>INVOICE				PROGRESS	

PROJECT DELIVERABLES				BUDGET			MATERIAL				MAN	MACHINERY	ACTUAL	COLLECTED	ACTUAL		
PROJECTDETIC	BOQ NO	BBU/BOQ ITEM	DEPARTMENT/DISCIPLINE	QTY	UNIT	RATE	EST AMOUNT	PLANNING	ORDERING	RECEIPT	ISSUES(DPR)	ATTENDANCE	USAGE	COST	AMOUNT	PROFIT	
1	1.1	DRAWING	ENGINEERING/PROCESS	1	DWG	200000	200000	EQUIPLIST	DCI>MR			HO	NIL	180000	300000	120000	
2	1.2	DOSING PUMP	PROCUREMENT/MECHANICAL	10	NOS	5000	50000	MR>PR	PO/WO(FG)	MIR/PI	MIN/DC	HO	NIL	55000	100000	45000	
3	1.4	VESSEL	MANUFACTURING/FACTORY	1	NOS	50000	50000	MR>PR(RM)	PO(RM)	MIR/PI	MFGORDER/DC	FACTORY	YES	40000	100000	60000	
4	1.3	FOUNDATION	CONSTRUCTION/CIVIL	100	SQFT	1000	100000	MR>PR	PO(BULK RM)	MIR/PI	MIN/DC	SITE	BATCH PLANT	80000	300000	220000	
5	1.5	VESSEL	ERECTION/COMMISSIONING	1	NOS	40000	40000	MR>PR	WO(FG)	MIR/PI	MIN/DC	SITE	YES	40000	50000	10000	
6	XX	MARKETING	MARKETING	1	NOS	10000	10000	SO(FG)	PO(RM)	MIR/PI	MFGORDER/DC	HO	NIL	9000	20000	11000	
							450000							404000	870000	466000	
													SAVINGS		46000		

DHIRALI MAMTA PREETI KOMAL & DIPMALA

DCR – DAILY CONSUMPTION REPORT

DMR – DAILY MACHINERY REPORT

DLR – DAILY LABOUR REPORT

Login to System

Login to ERP

Enter your username...

Enter your password...

Year: 2324 ▾

Company: Paramount Limited ▾

Project Code: 0

Login

Best with:
Microsoft Edge v 11
IEv11-EIE11_EN-US_MCM_WIN764
Android Mobile

Licensed by MobileERP.in



PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10

Attendance 3 4 5

3a 3b 3c

Vendor Labour Staff

Work Created By: Niravsir 1b,c Create
BBU Item: Building 4
BBU Activity: Construction

Chotturam 2 Update
Brick Work 30/1k sqft

Ramchand Update
Plumbing Work 10/80 sqft

Unassigned Update
Electrical Work 200/600m

1a

+ ToDo Doing Reports

STEP 1: CREATE WORK

a. Select BBU Item to work with

PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10

Inprogress Tasks List Search..

DoWork Done

3416. IOCL Pre-Design-DCI
 IOCL(Gujarat Refinery)
 Issue of Approved Document to concerned department
 PL: LUPEC
 Dueon: 03/05/2022 12:41:17
 Plan: 1 Days 1 Hrs
 Delay: 308 days

DoWork Done

3417. IOCL Pre-Design-DCI
 IOCL(Gujarat Refinery)
 Preparation of MR
 PL: LUPEC
 Dueon: 07/05/2022 11:17:43
 Plan: 1 Days 1 Hrs
 Delay: 308 days

DoWork Done

+ ToDo Doing Reports

b. See progress of work + create+update

PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10

Attendance

Vendor Labour Staff

Work Created By: Niravsir
 BBU Item: Building 4
 BBU Activity: Construction **Create**

Chotturam
Brick Work 30/1k sqft **Update**

Ramchand
Plumbing Work 10/80 sqft **Update**

Unassigned
Electrical Work 200/600m **Update**

+ ToDo Doing Reports

TOMMORROWS PROGRAM			
SR NO	ITEM NO	DESCRIPTION	LOCATION
1	House Keeping		ETP & HWHF
2	Soil dressing for pavent area		ETP
3	Hydro testing work		ETP

c. Enter + assign work for today or tomm.

Work Created By: Niravsir **Not Started**
 BBU Item: Building 4
 BBU Activity: Construction

Work details

Work Name
 Brick Work

Total Work
 0

Unit
 Kg

Assigned To
 Lallan

Subcontractor name
 Chottan Thakur

STEP 2: ENTER WORKDONE

a. Enter today's work done by subcon

b. Check entire work done by subcon

A. WORK DONE

B.O.Q. No.	Item	Total Qty.	Done Today	Done Till Today
	SBR stair case		2 cum	
	HRSCC channel		2 cum	
	ORC Foundation 2		3 cum	
	SS building		2cum	
	Hydro testing work			
	Earth work for pavement			
	SS building misc civil work			
	Block work & plaster			
	shuttering & reinforcement work various structure			

F. DECISIONS HOLDING UP WORKS


Description	To be given by	Date Required

B. PLANNED WORKS NOT EXECUTED

Sr. No.	Item	Reason why not executed

PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10



Chotturam Doing
 Subcon: Lallan
Brick Work 30/1k sqft

Today's Work Update

Progress (Qty)
0.00

Unit
Kg


No of labour working
0

Add Photo filename

Remarks


PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10




Chotturam Doing
 Subcon: Lallan
Brick Work 30/1k sqft

Work Done Status Messages



Work assigned by Niravsir
11/04.2023 11:00



Today's Progress - 3 mt/100
 Labour Present - 40
 11/04.2023 11:01

+
ToDo

♥
Doing

🔍
Reports

Step 3a: Manpower Attendance Entry

E. MANPOWER						
Supervisor	Masons	Carpenters	Other Skilled Workers	Male Helpers	Female Helpers	Total
2	10	32	13	27	0	84

Contract Labour

PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10

Total 12 10 10 8 12000

Date: dd-mm-yyyy

Labour: UnSkilled SemiSkilled Skilled Highly Skilled

Gender: Male Female

No. of Labour Present: Member

Daily Wages: wages/day

Add Photo filename: proof.png

Remarks: Add comments

Save and Update

+ ToDo Doing Reports

Department Labour

PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10

Own Labour Attendance

RCM@Site: Ramesh List

Date: dd-mm-yyyy

Labour	Present	Absent
Lallan	<input checked="" type="radio"/>	<input type="radio"/>
Chotu	<input checked="" type="radio"/>	<input type="radio"/>
Total	2	0

Remarks: Add comments

+ ToDo Doing Reports

Staff Employee

PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10

Hardik Attendance

Punch In Punch Out

MONTH: 3 YEAR: 2023 Go

30 Mar 2023 Absent

In : Out :

29 Mar 2023 Present

In : 10:57:00 Out : 19:00:00

+ ToDo Doing Reports

Step 3b: Manpower Musteroll

E. MANPOWER						
Supervisor	Masons	Carpenters	Other Skilled Workers	Male Helpers	Female Helpers	Total
2	10	32	13	27	0	84

PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10

Vendor Labour Attendance

Vendor/Contractor: Lallan [List](#)

Gender	UnSki	Semi	Skil	HSki	Pay
Male	3	5	8	8	7000
Female	9	5	2	0	5000
Total	12	10	10	8	12000

Date:

Labour: UnSkilled SemiSkilled Skilled Highly Skilled

Gender: Male Female

[+](#) [ToDo](#) [Doing](#) [Reports](#)

PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10

Own Labour Attendance

RCM@Site: Ramesh [List](#)

Date:

Labour	Present	Absent
Lallan	<input checked="" type="radio"/>	<input type="radio"/>
Chotu	<input checked="" type="radio"/>	<input type="radio"/>
Total	2	0

Remarks:

[+](#) [ToDo](#) [Doing](#) [Reports](#)

PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10

My Attendance Record

MONTH	Present	Absent	Leave	Paydays
OCT	26	0	0	26
SEP	26	0	0	26
AUG	26	0	0	26
JLY	23	3	1	24
JUN	26	0	0	26
MAY	26	0	0	26
APR	24	0	0	26
MAR	26	0	0	26
FEB	25	0	0	26
JAN	26	0	0	26


Total Working Days: 210

[+](#) [ToDo](#) [Doing](#) [Reports](#)

STEP 4a: Enter Material Receipt

I. MATERIAL RECEIVED

	Item	Unit	Qty.
1	Drill Bit	nos	2

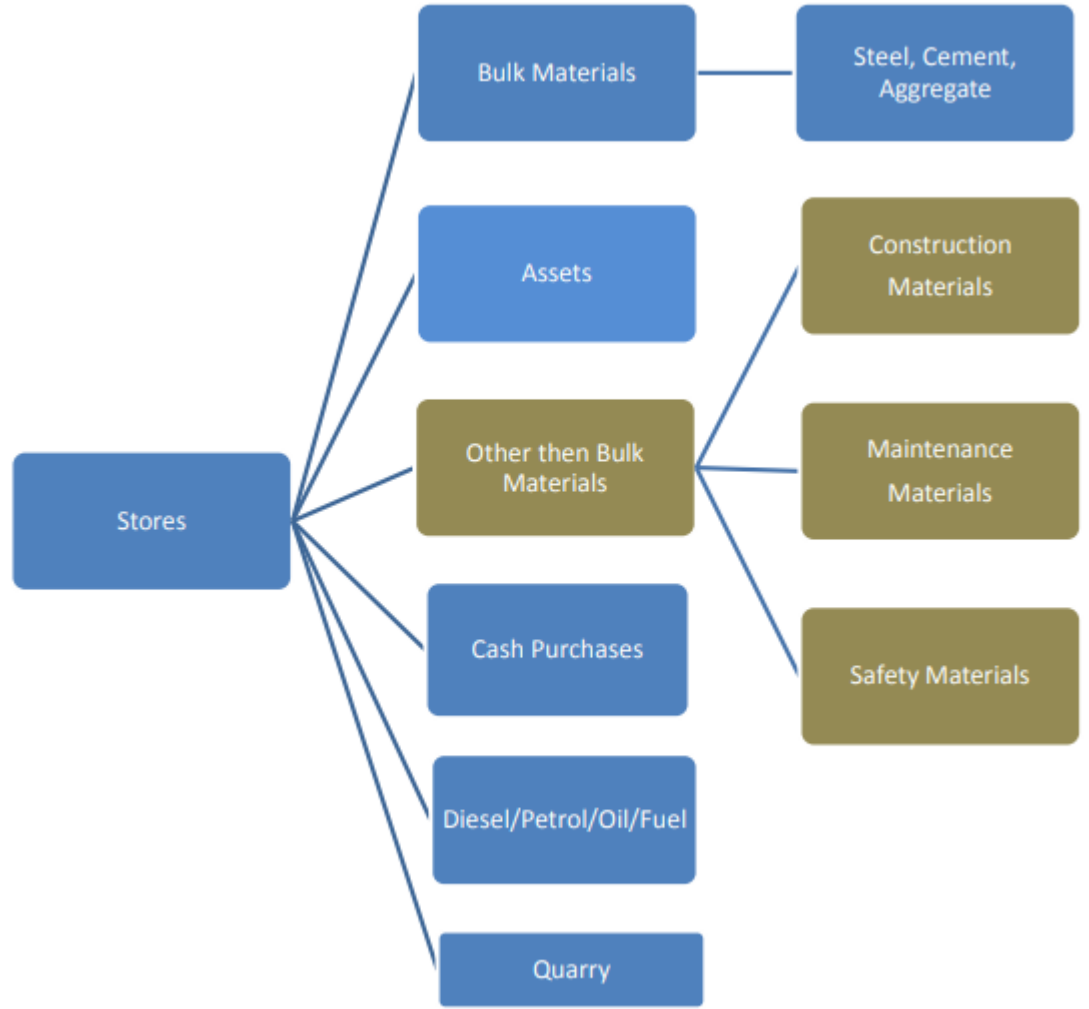

☰ PROJECT: PL631 HRRL

MAN 30
MATERIAL 20
MACHINERY 10

GRN: Material Received

Request
Ordered
Received

Storekeeper: Ramanji

Last updated 11/04.2023 11:00

Cement - 30 bags

Stock: 400 bags
Rcvd against PO: 678
11/04.2023 11:01

Bricks - 400 nos

Stock: 900 nos
Rcvd against PO: 678

+
+ ♥ 🔍

STEP 4b: Enter Material Issue

DCR FOR MATERIAL USED IN PRODUCTION

K . MATERIAL CONSUMED AT SITE TODAY (VERY IMPORTANT)

B.O.Q. No.	BOQ QTY	Material	Unit	Qty. Issued	STOCK
		Sand	cum	3.6	650 MT
		aggregate	cum	5.4	600 MT
		cement	kg	4050	55 MT
		Alcofine			30 MT
		Binding wi	kg	10	520 KG
		Nails	kg	4	50 KG

DCR FOR MATERIAL USED IN MACHINERY

Diesel STOCK FOR Dhandholi FROM 1/6/2011 TO 1/6/2011

Opening Stock:
1175

Inward (Ltrs):
3760

Inward Details:

-Store 26994 3760

Total Stock:
4935

Issue (Ltrs):
2924

Closing Stock:
2011

ISSUE NO.	MACHINENAME	QTY	Reading	SLIPNO	SLIPDATE	SITE	PARTY	CHARGEABLE
0	-Generator Set	500	2368	28484	01/06/2011	Dhandholi	PIPL	False
1	-Bitumen Paver	125	6216	28485	01/06/2011	Dhandholi	PIPL	False
2	Maintenance (D.B.M.)-	5	0	28486	01/06/2011	Dhandholi	PIPL	False
3	-Roller	30	6577	28487	01/06/2011	Dhandholi	PIPL	False
4	-PTR	45	686	28488	01/06/2011	Dhandholi	PIPL	False
5	HM Loader (NEW 3)-	168	1078	28489	01/06/2011	Dhandholi	PIPL	False
6	-Generator Set	125	3557	28490	01/06/2011	Dhandholi	PIPL	False
7	Dozar TD-9-	40	50	28491	01/06/2011	Dhandholi	PIPL	False
8	-Motor Grader	184	2089	28492	01/06/2011	Dhandholi	PIPL	False
9	-Soil Compactor	102	1603	28493	01/06/2011	Dhandholi	PIPL	False
10	-Motor Grader	136	1928	28494	01/06/2011	Dhandholi	PIPL	False
11	-Bitumen Paver(Ap 755)	77	3058	28495	01/06/2011	Dhandholi	PIPL	False
12	-Generator Set	39	2675	28496	01/06/2011	Dhandholi	PIPL	False
13	HM Loader (NEW)-	130	2076	28497	01/06/2011	Dhandholi	PIPL	False
14	RJ36 TA 0001-	50	2833	28498	01/06/2011	Dhandholi	Shubham Construction	False
15	-Loader	168	8678	28499	01/06/2011	Dhandholi	PIPL	False
16	Excavator L&T PC 200-	162	3213	28500	01/06/2011	Dhandholi	PIPL	False
17	Boiler Hot Mix Plant-	239	254	28501	01/06/2011	Dhandholi	PIPL	False
18	-Generator Set	39	4657	28502	01/06/2011	Dhandholi	PIPL	False
19	-Generator Set	500	2377	28503	01/06/2011	Dhandholi	PIPL	False

PROJECT: PL631 HRRL

MAN 30
MATERIAL 20
MACHINERY 10

Chotturam

Subcon: Lallan

Brick Work 30/1k sqft

List

Today's Material Issue

Material

Qty

Unit

Please fill out this field.

Issued To

Add Photo filename

+
ToDo

♥
Doing

🔍
Reports

STEP 4c: Manage Material Inventory

PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10

Work Created By: Niravsir
BBU Item: Building 4
BBU Activity: Construction Inventory

Chotturam
Brick Work 30/1k sqft Issue

Ramchand
Plumbing Work 10/80 sqft Issue

Unassigned
Electrical Work 200/600m Issue

+
+ ToDo ❤️ Doing 🔍 Reports

PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10

Inventory

PR PO GRN MIN

Storekeeper: Ramanji
Last updated 11/04.2023 11:00

Material	PR	PO	GRN	MIN	STK
Cement Bgs	3	5	8	8	0
Bricks Nos	9	5	2	0	2
Sand MT	12	10	30	10	20





+
+ ToDo ❤️ Doing 🔍 Reports

STEP 5: Machinery Usage Entry

C. PLANT AT SITE		D. PLANT REQUIRED BUT NOT AT SITE	
Item	Working Condition	Item	Date Required
BATCHING PLANT	OK		

PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10

- Machinery
- 
 Work Created By: Niravsir
 BBU Item: Building 4
 BBU Activity: Construction
 - 
 Chotturam
Brick Work 30/1k sqft
 - 
 Ramchand
Plumbing Work 10/80 sqft
 - 
 Unassigned
Electrical Work 200/600m

Omkareshwar Camp Time Log Sheet

Period From 1/10/2010 to 18/01/2011

HYWA TIPPER/9733--(TIPPER/9733)--(TIPPER/9733)

Print Date 18/01/2011 12:53:10

Date	Work Mode	Starting	Closing	TOTAL	NW Hr	Description	Diesel (Qty)	MR No
09/10/2010	Working	2586.6	2603	16.40000000000001	0	LOADING AND UNLOADING WORK AT SITE	0	
11/10/2010	Working	2622.8	2634.1	11.299999999999997	0	MATERIAL LOADING AND DUMPING AT SITE CH.144.450 TO 144.500 TOTAL 18 TRIP	0	
13/10/2010	Working	2659.2	2690.8	31.600000000000004	0	LOADING AND UNLOADING WORK AT SITE 10 TRIPS	0	
14/10/2010	Working	2690.8	2726	35.199999999999998	0	MATERIAL LOADING AND UNLOADING AT SITE	0	
15/10/2010	Working	2726	2779.7	53.699999999999998	0	CH.160.010(V.R.B)MATERIAL LOADING AND UNLOADING AT SITE MATERIAL LOADING TRIP= 2 TO 144.600	0	
24/10/2010	Working	2910.1	2917.3	7.2000000000000027	0	loading ch. 147.850 to 147.99 146.910 i.p. side	0	
25/10/2010	Working	2917.3	2989.1	71.799999999999997	0	162.400 to 162.030 road filling	0	
26/10/2010	Working	2947.3	3013.9	66.599999999999999	0	162.400 and 162.300 cutting a	0	
Total				293.8	0			

Summary


Work Mode (Per KM)	Total
Working	293.8
Idle	0
BreakDown	0
ShutDown	0
Diesel Issued	0
Diesel Avg	0
Working Days	8
Total Days	8

PROJECT: PL631 HRRL

MAN 30 MATERIAL 20 MACHINERY 10

Machinery

Request Ordered Received


 Storekeeper: Ramanji
 Last updated 11/04.2023 11:00

Truck - 2km/3hrs

Issued to Choturam on 11/04.2023 11:01

Batching Plant - 2hrs
